


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Jan 10, '16							Jan 17, '16						
							S	M	T	W	T	F	S	S	M	T	W	T	F	S
1		<b>Robot 1</b>	<b>13.75 days</b>	<b>Mon 1/11/16</b>	<b>Sat 2/13/16</b>															
2		<b>Drive Train/Chassis</b>	<b>10.5 days</b>	<b>Mon 1/11/16</b>	<b>Fri 2/5/16</b>															
3		Design Concept	9 hrs	Mon 1/11/16	Thu 1/14/16															
4		Build Prototype	6 hrs	Mon 1/11/16	Tue 1/12/16															
5		Detailed Design (CAD)	46 hrs	Fri 1/15/16	Tue 1/26/16	3														
6		Build	9 hrs	Thu 1/28/16	Sat 1/30/16	5														
7		Assemble	20 hrs	Sat 1/30/16	Fri 2/5/16	6														
8		<b>Shooter</b>	<b>12.63 days</b>	<b>Mon 1/11/16</b>	<b>Tue 2/9/16</b>															
9		Prototyping	12 hrs	Mon 1/11/16	Fri 1/15/16															
10		Detailed Design (CAD)	26 hrs	Sat 1/16/16	Fri 1/22/16	9														
11		Second Prototype	20 hrs	Sat 1/23/16	Thu 1/28/16	10														
12		Build	11 hrs	Fri 1/29/16	Sun 1/31/16	11,18														
13		Assemble	9.5 hrs	Sun 1/31/16	Thu 2/4/16	12														

Project: Build Plan  
Date: Tue 2/23/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Jan 10, '16							Jan 17, '16						
							S	M	T	W	T	F	S	S	M	T	W	T	F	S
14		Mount/Install	6 hrs	Mon 2/8/16	Tue 2/9/16	2,13,23,24														
15		<b>Loader</b>	<b>11.13 days</b>	<b>Sat 1/16/16</b>	<b>Tue 2/9/16</b>															
16		Design Concept	12 hrs	Sat 1/16/16	Sun 1/17/16	9														
17		Detailed Design (CAD)	12 hrs	Sun 1/17/16	Fri 1/22/16	16														
18		Prototype	11 hrs	Fri 1/22/16	Sun 1/24/16	17														
19		Build	11 hrs	Fri 1/29/16	Sun 1/31/16	17,18,11														
20		Assemble	9.5 hrs	Sun 1/31/16	Thu 2/4/16	19														
21		Mount/Install	6 hrs	Mon 2/8/16	Tue 2/9/16	2,20,23,24														
22		Bumpers	14.5 hrs	Thu 1/28/16	Sun 1/31/16	5														
23		Testing of Drive Train	8 hrs	Sat 2/6/16	Sun 2/7/16	7,42														
24		Ruggedness Testing	3 hrs	Sun 2/7/16	Sun 2/7/16	23														
25		Integration Testing of Robot	9 hrs	Thu 2/11/16	Sat 2/13/16	7,14,21,42,43,44,														
26		<b>Robot 2</b>	<b>10.31 days</b>	<b>Mon 2/8/16</b>	<b>Sun 2/28/16</b>															

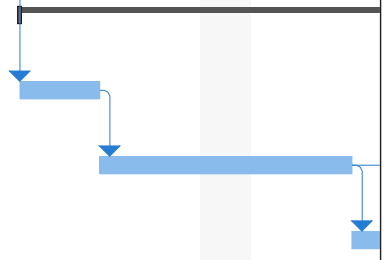

Project: Build Plan  
Date: Tue 2/23/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Jan 10, '16							Jan 17, '16						
							S	M	T	W	T	F	S	S	M	T	W	T	F	S
27		<b>Drive Train/Chassis</b>	<b>8.75 days</b>	<b>Mon 2/8/16</b>	<b>Sun 2/21/16</b>															
28		Build	11 hrs	Tue 2/16/16	Thu 2/18/16	7,24														
29		Assemble	16 hrs	Thu 2/18/16	Sun 2/21/16	28														
30		<b>Shooter</b>	<b>7.56 days</b>	<b>Thu 2/11/16</b>	<b>Tue 2/23/16</b>															
31		Build	11 hrs	Thu 2/11/16	Sat 2/13/16	14														
32		Assemble	6 hrs	Sat 2/20/16	Sat 2/20/16	31														
33		Mount/Install	3 hrs	Tue 2/23/16	Tue 2/23/16	32,29														
34		<b>Loader</b>	<b>6.19 days</b>	<b>Thu 2/18/16</b>	<b>Sun 2/28/16</b>															
35		Build	11 hrs	Thu 2/18/16	Sat 2/20/16	21														
36		Assemble	6 hrs	Sat 2/20/16	Sun 2/21/16	35														
37		Mount/Install	3 hrs	Tue 2/23/16	Tue 2/23/16	36,29														
38		Bumpers	14.5 hrs	Tue 2/23/16	Sat 2/27/16	5														
39		Integration Testing of Robot	6 hrs	Thu 2/25/16	Fri 2/26/16	29,33,37,42,43,44														


Project: Build Plan Date: Tue 2/23/16	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Jan 10, '16							Jan 17, '16							
							S	M	T	W	T	F	S	S	M	T	W	T	F	S	
40		<b>Software</b>	<b>17.88 days</b>	<b>Mon 1/11/16</b>	<b>Fri 2/19/16</b>																
41		Planing	18 hrs	Mon 1/11/16	Sat 1/16/16																
42		Code Drive Train	6 hrs	Sun 1/17/16	Sun 1/17/16	41															
43		Code Shooter	6 hrs	Sun 1/17/16	Sun 1/17/16	41															
44		Code Loader	6 hrs	Sun 1/17/16	Sun 1/17/16	41															
45		<b>Vision</b>	<b>5.56 days</b>	<b>Sun 1/17/16</b>	<b>Sat 1/30/16</b>	<b>41</b>															
46		Co-Processor	29.5 hrs	Sun 1/17/16	Sun 1/24/16																
47		Target Recognition	9 hrs	Sun 1/24/16	Thu 1/28/16	46															
48		Auto Targeting	6 hrs	Thu 1/28/16	Sat 1/30/16	47															
49		Drive Station	6 hrs	Sun 1/17/16	Tue 1/19/16	42,43,44															
50		Code Auto Period	9 hrs	Sat 1/30/16	Sun 1/31/16	5,43,44,45															
51		Code Teleop	3 hrs	Thu 1/28/16	Thu 1/28/16	5															
52		Driver Acceptance Testing of Teleop	3 hrs	Sat 2/13/16	Sat 2/13/16	25,51															


Project: Build Plan  
Date: Tue 2/23/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Jan 10, '16							Jan 17, '16												
							S	M	T	W	T	F	S	S	M	T	W	T	F	S						
53			Integration Testing of Auto	30 hrs	Sun 2/14/16	Fri 2/19/16	25,52																			
54			Driver Training	30 hrs	Thu 2/18/16	Sat 2/27/16	52																			
55			Test Drive Train Prototype	3 hrs	Thu 1/14/16	Thu 1/14/16	4																			




Project: Build Plan Date: Tue 2/23/16	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

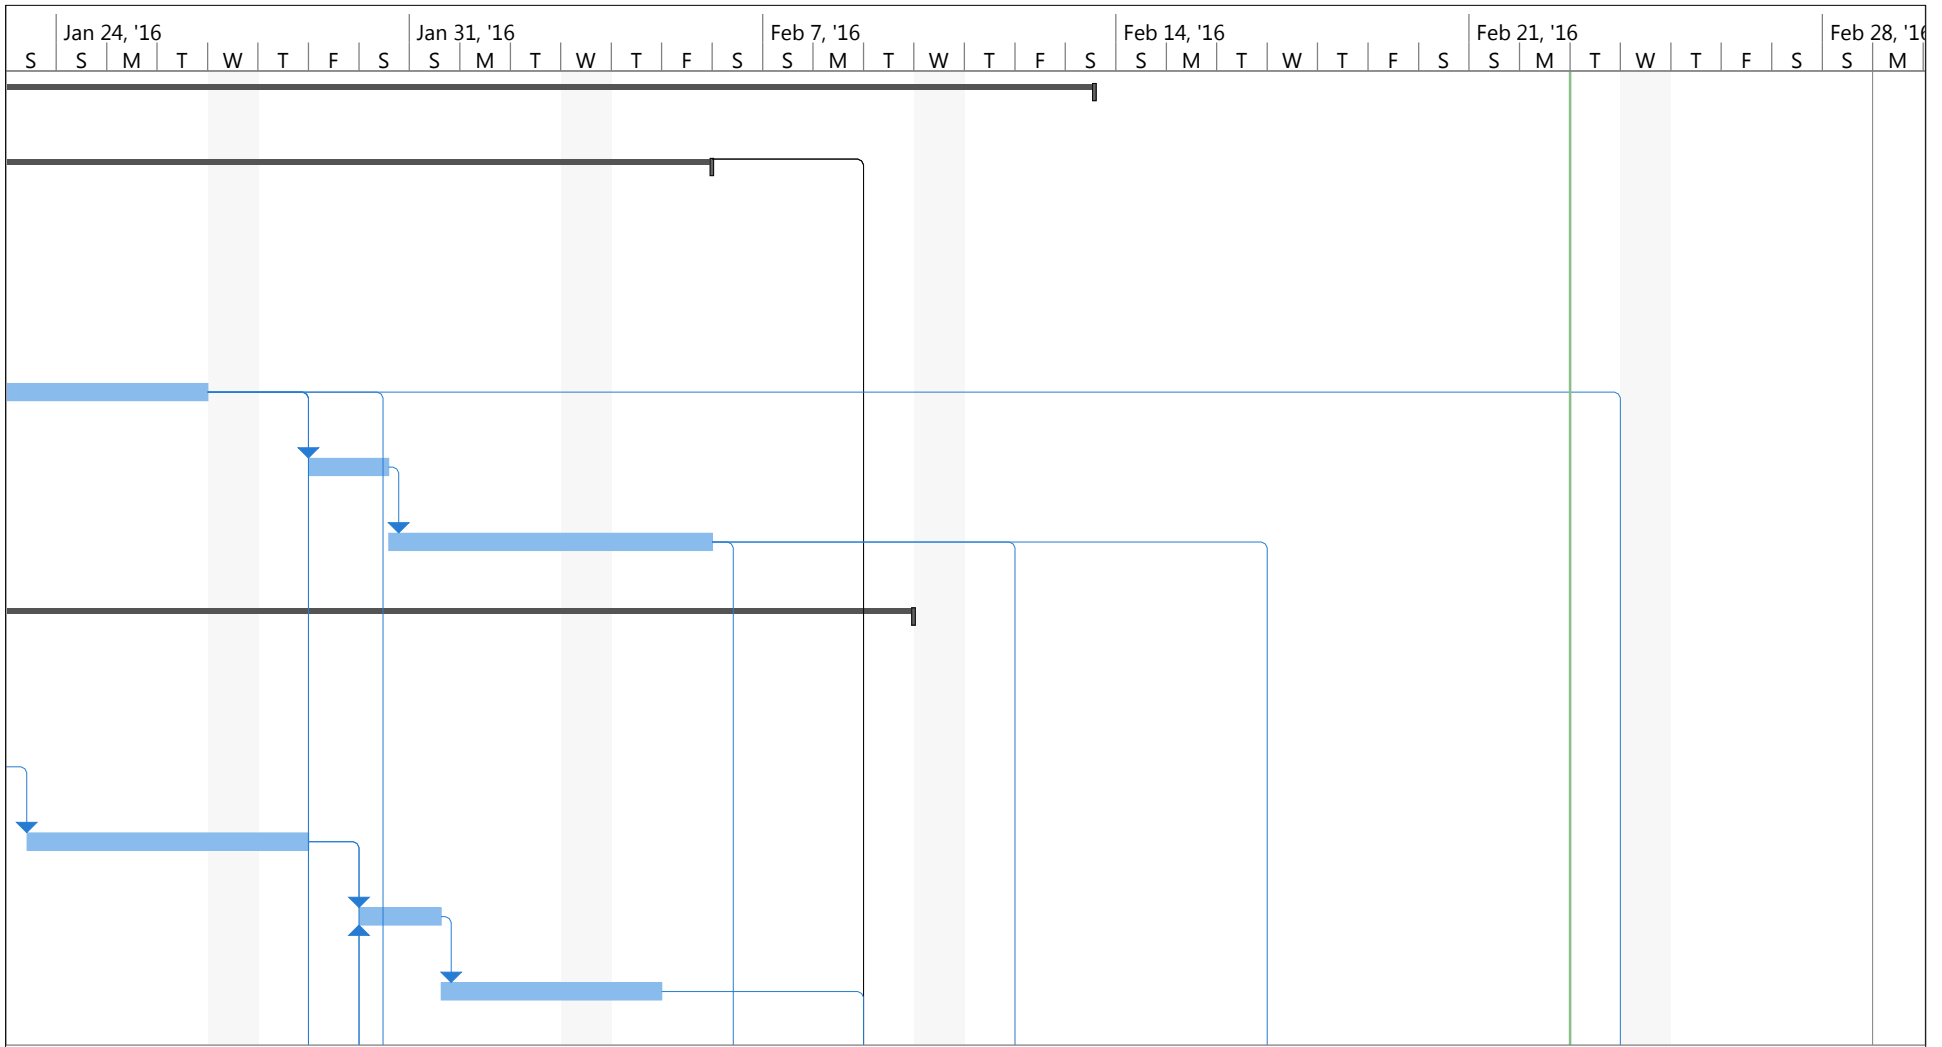


Project: Build Plan  
Date: Tue 2/23/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

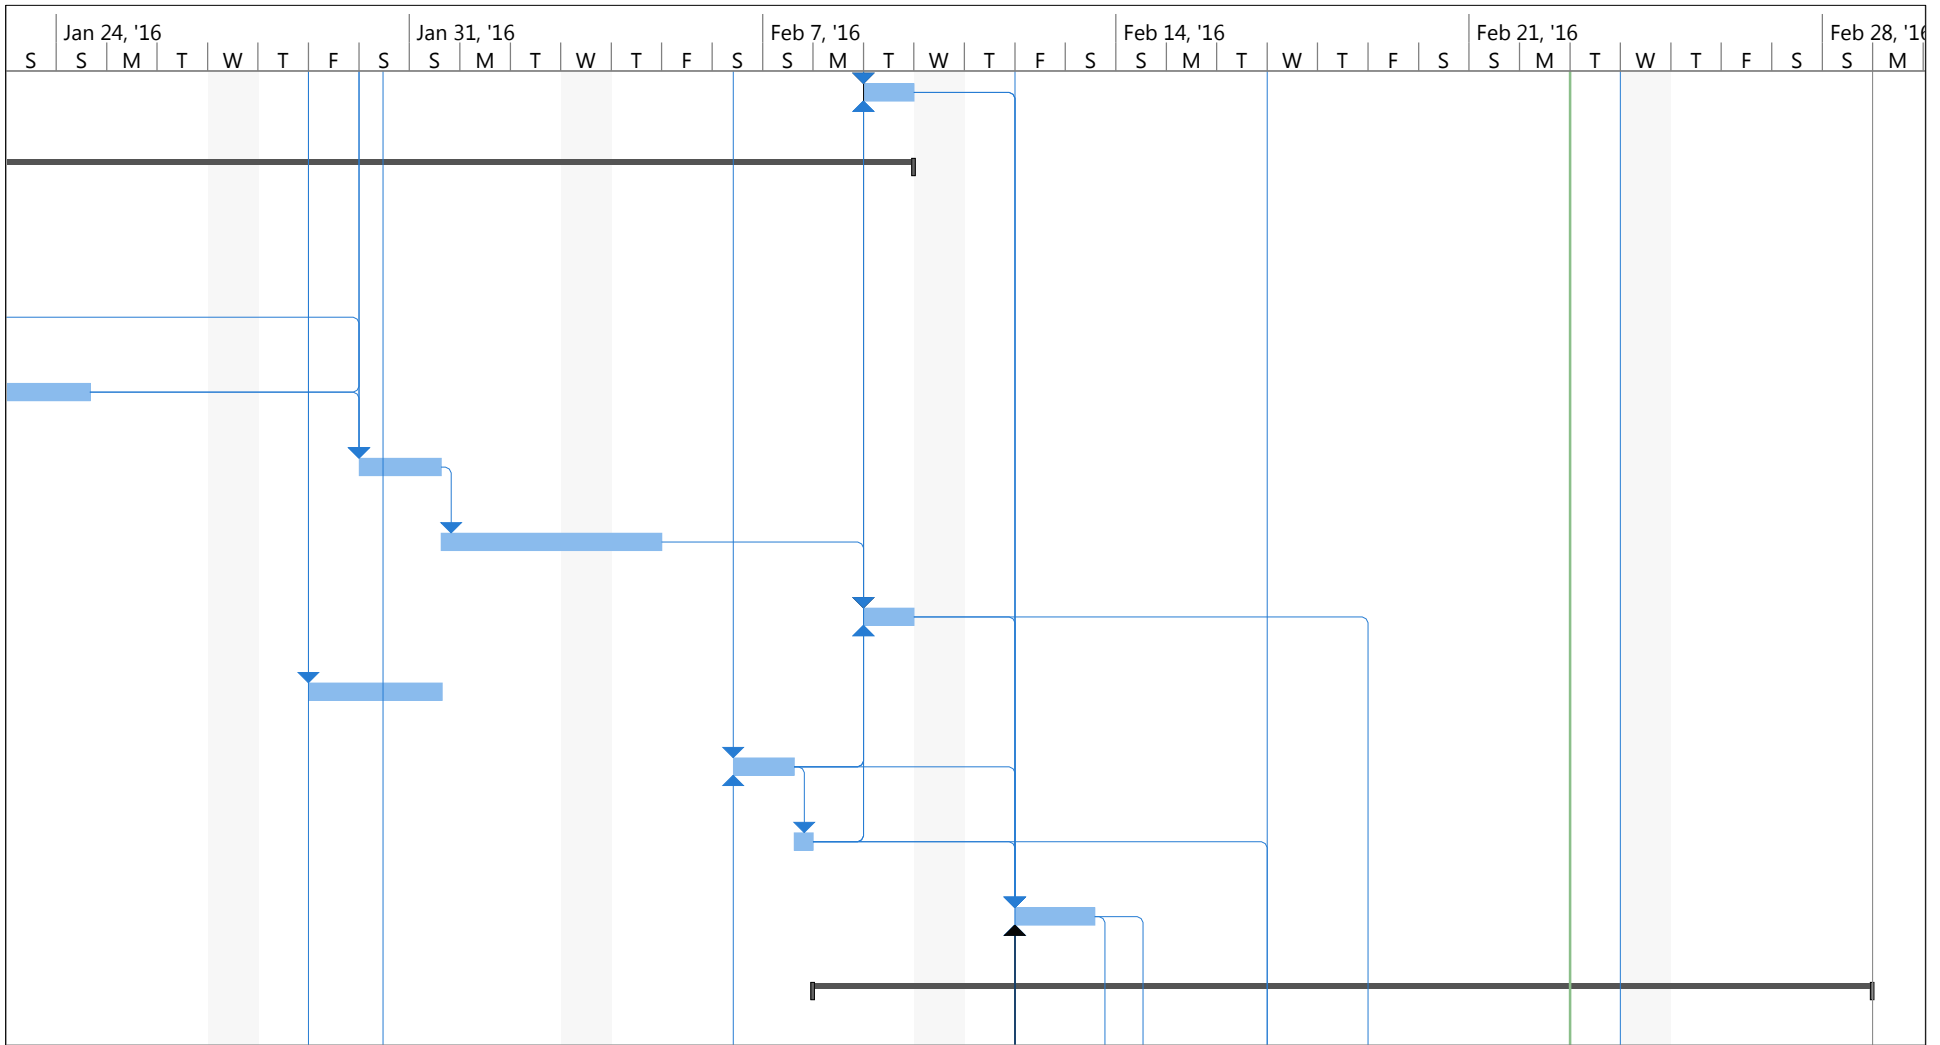


Project: Build Plan Date: Tue 2/23/16	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

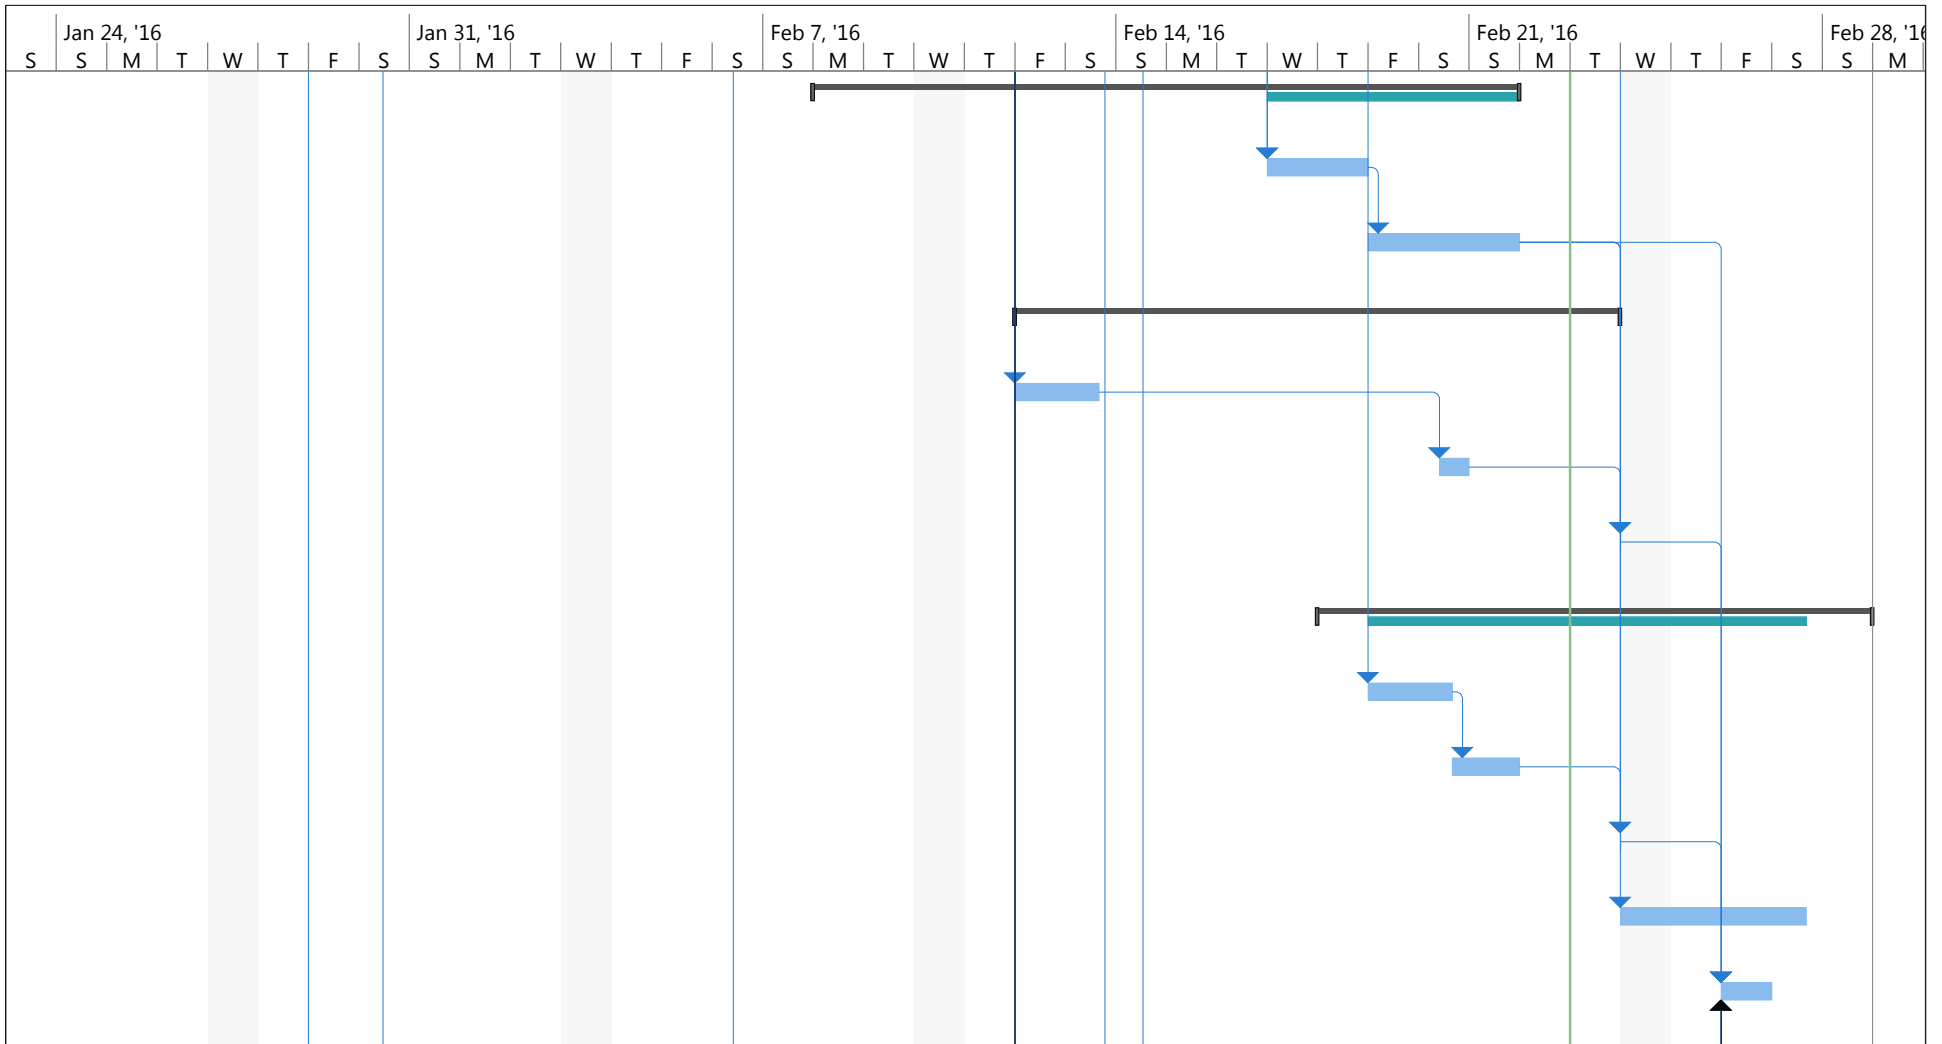


Project: Build Plan Date: Tue 2/23/16	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



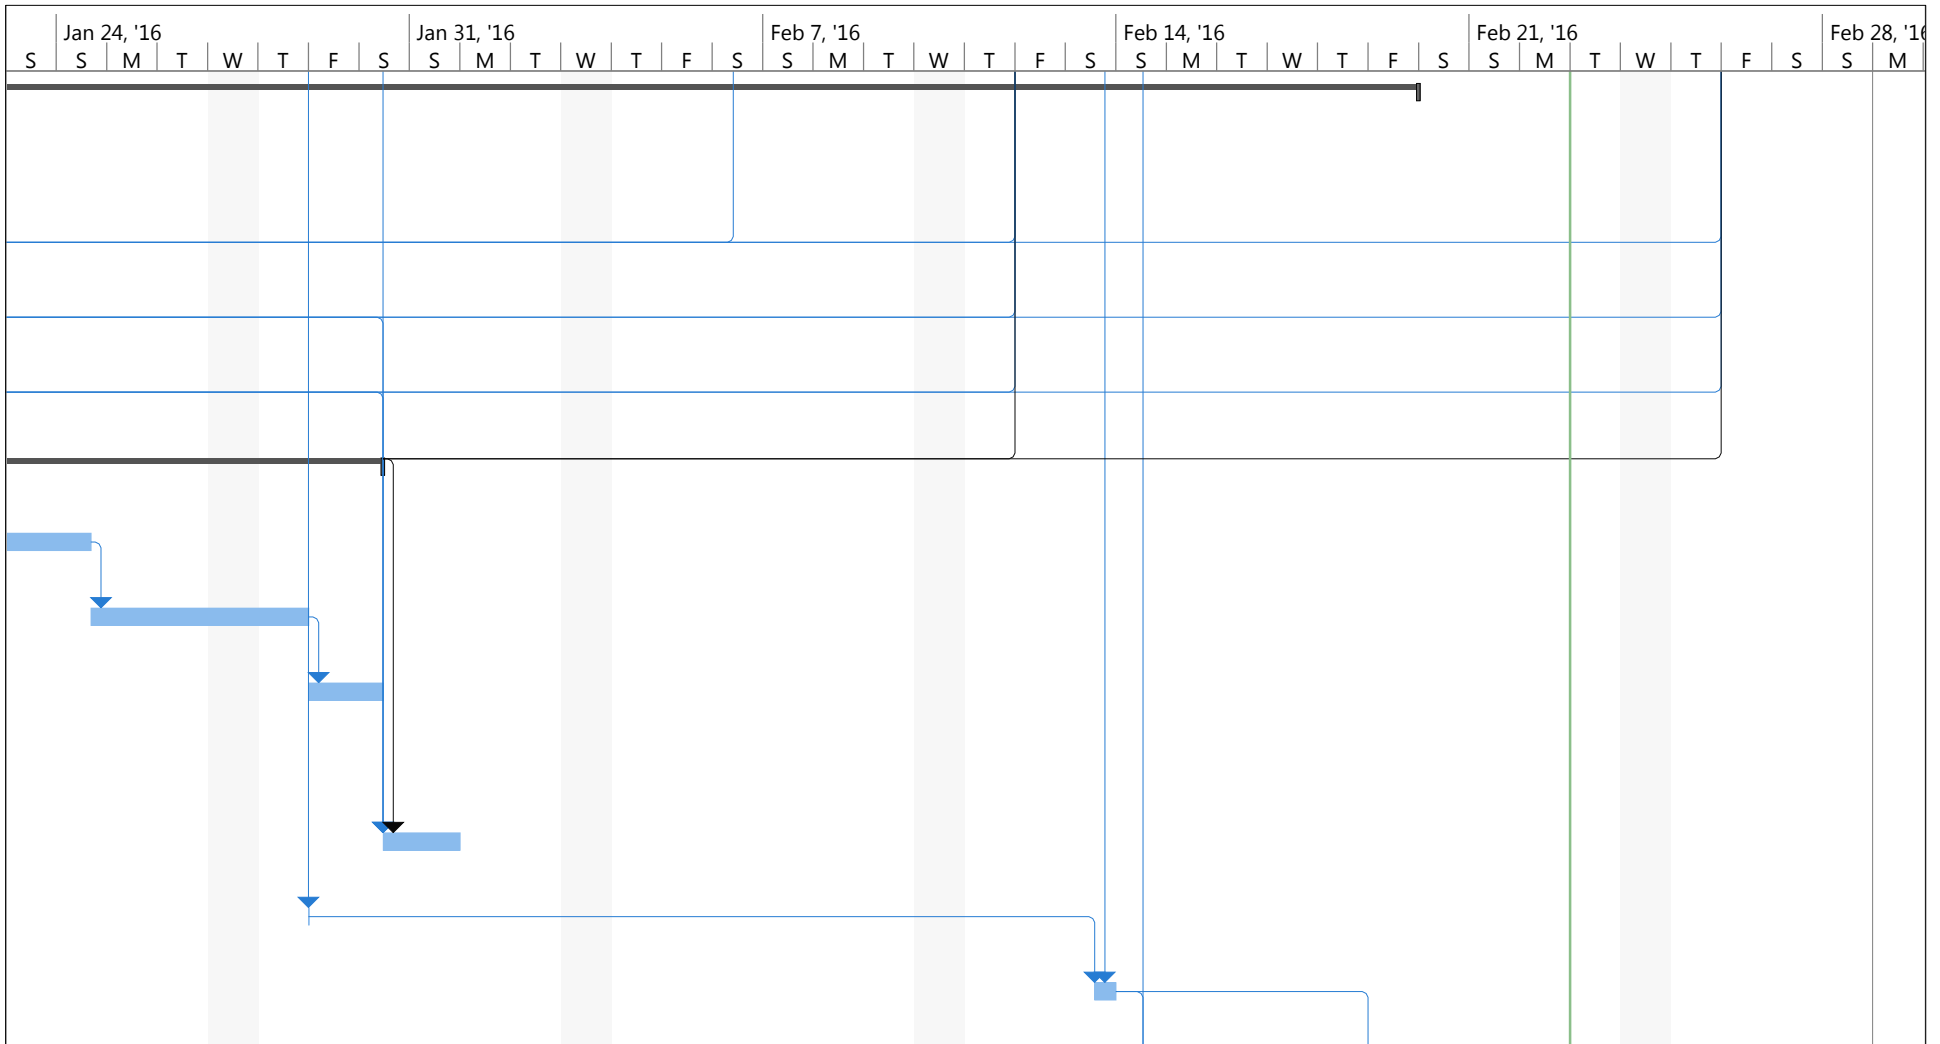

Project: Build Plan  
Date: Tue 2/23/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

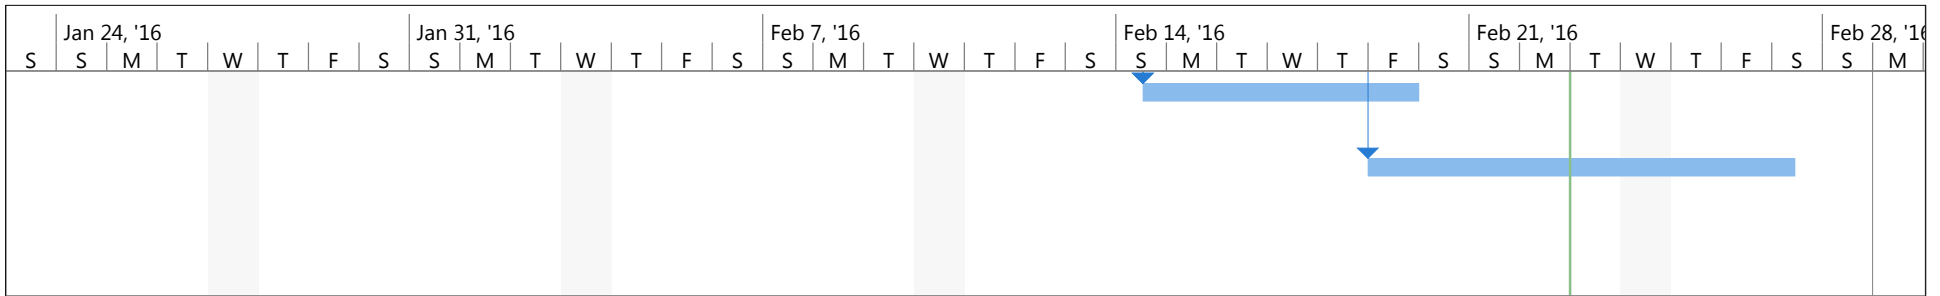

Project: Build Plan Date: Tue 2/23/16	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			
